

TRAFFIC MANAGEMENT PLAN

**EAST SIDE ELEMENTARY
10125 McGrath Road,
Chilliwack, BC**

Table of Contents

1.0	Introduction.....	3
2.0	Scope of Work	3
3.0	Hours of Work	3
4.0	Staging Areas.....	3
5.0	Emergency Vehicle Access.....	3
6.0	Road Debris	3
7.0	Traffic Signage	4
8.0	Traffic Control Plans	4

1.0 Introduction

This Traffic Management Plan has been prepared by Metric Civil Contractors Ltd. (Metric Civil) to support the off-site construction activities associated with the East Side Elementary project located at 10125 McGrath Road, Chilliwack, BC

2.0 Scope of Work

The Scope of Work includes, but is not limited to:

- Telus and BC Hydro Works

CONTACT NAME	POSITION	PHONE NUMBER	E-MAIL
Saif Saifuzzaman	Project Manager	(778) 325-5159	saif@metriccivil.ca
Suruchi Sharma	Project Coordinator	(587) 889-6742	suruchi@metriccivil.ca
Jeff Hutt	Operations Manager	604) 845-7171	jeff@metriccivil.ca
Mike Hill	General Superintendent	(604) 991-1261	mike.hill@metriccivil.ca

3.0 Hours of Work

The expected hours of work 7:00 AM to 5:00 PM.

4.0 Staging Areas

All materials such as gravel, pipe, precast concrete will be staged on-site only. Public Roads will not be used for staging any materials for this project. Temporary modular fencing will be used on-site to separate the general work area from the public.

5.0 Emergency Vehicle Access

Emergency vehicle access will be maintained at all times for both the project area and any surrounding properties.

6.0 Road Debris

At all times during construction, Metric Civil shall ensure the road is clear of dirt, mud and rock debris. If any dirt, mud or debris leaves the work zone, Metric Civil will ensure that it is removed immediately.

7.0 Traffic Signage

Traffic signage will be placed notifying the public of construction traffic. The signs will be placed for both east and west bound traffic.

8.0 Traffic Control Plans

The following Ministry of Transportation and Infrastructure figure will be used for traffic control during off-site construction activities:

- Figure 7.8 - Single Lane Alternating: to be used for any work between the hours of 7:00AM - 5:00PM

Figure 7.5: Work on Shoulder – Short and Long Duration

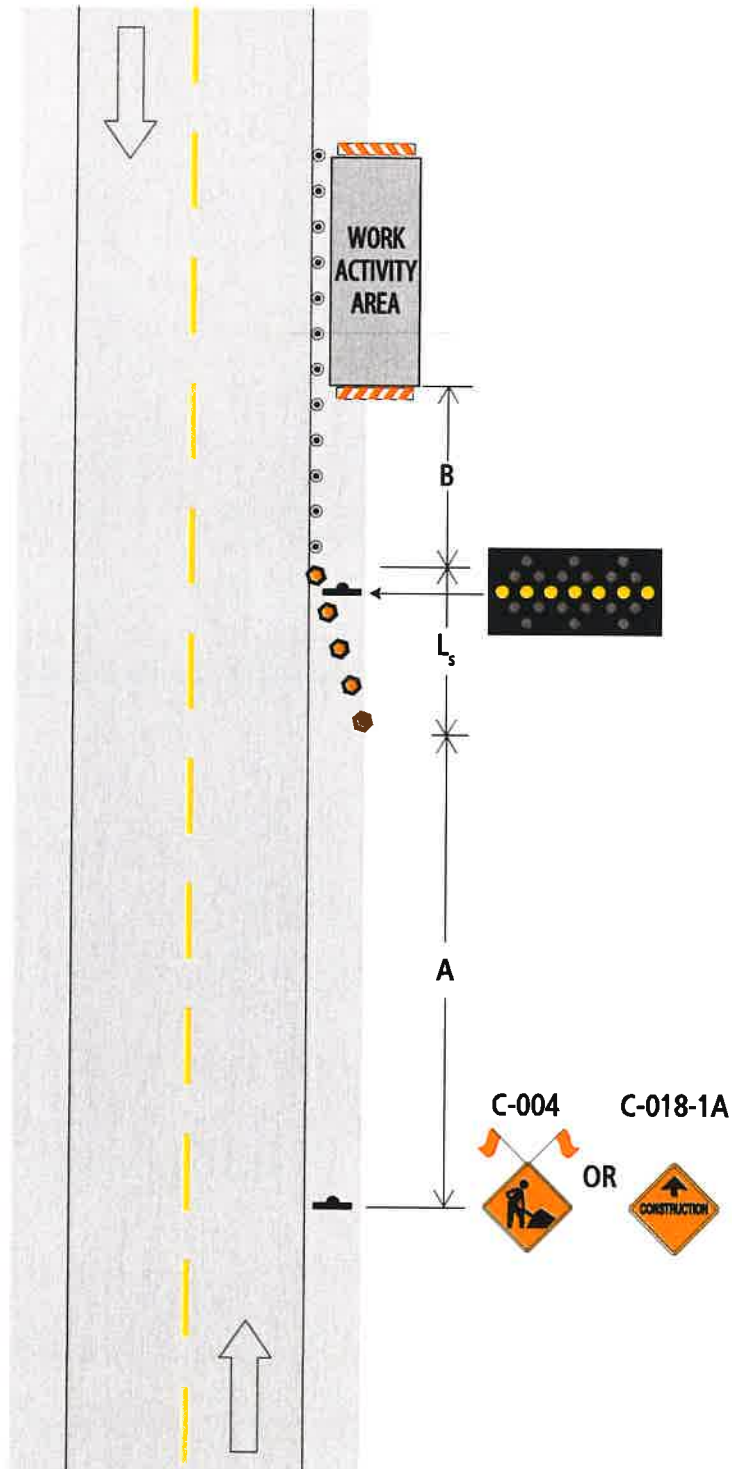


Figure 7.7: Roadside Work – Encroachment into Travel Lane – Short Duration

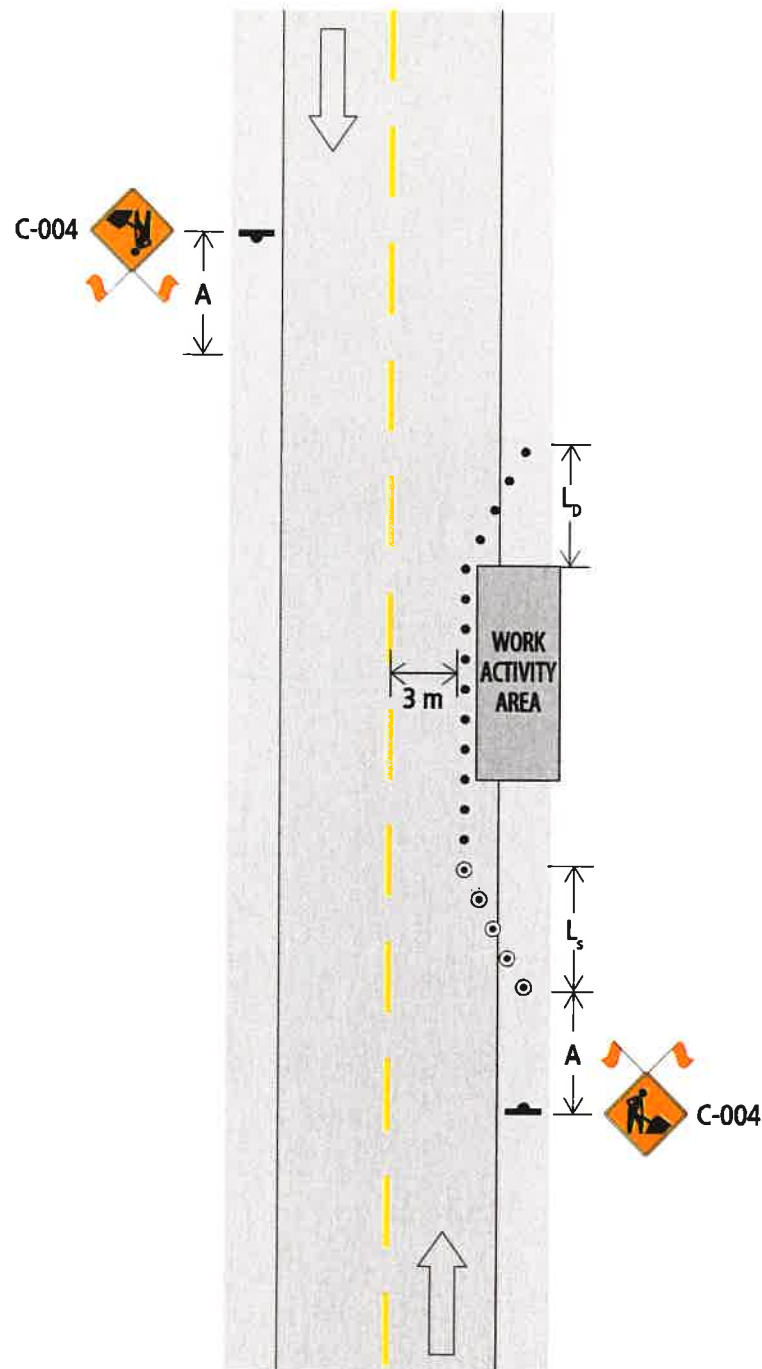


Figure 7.8: Lane Closure with TCPs – Single Lane Alternating – Short and Long Duration

