Date: Tues Sept 7, 2021 **Author:** Stephanie Charlie 604 Traffic LTD
Company: Universal Construction **Contact:** Jeff Boychuk (604)997-3750
Comments:

- Traffic Plan Based on Modi 2020 Fg. 8.6 right lane closed
- Traffic Plan based on 50 km/hr speed zone
- Traffic Plan conforms to Modi 2020 Specs
- TCP placed on Marie Ave to facilitate traffic heading North onto Vedder Rd
- TCP with the crew to help facilitate the traffic heading South
- TCP on West side will also assist pedestrians around the workzone

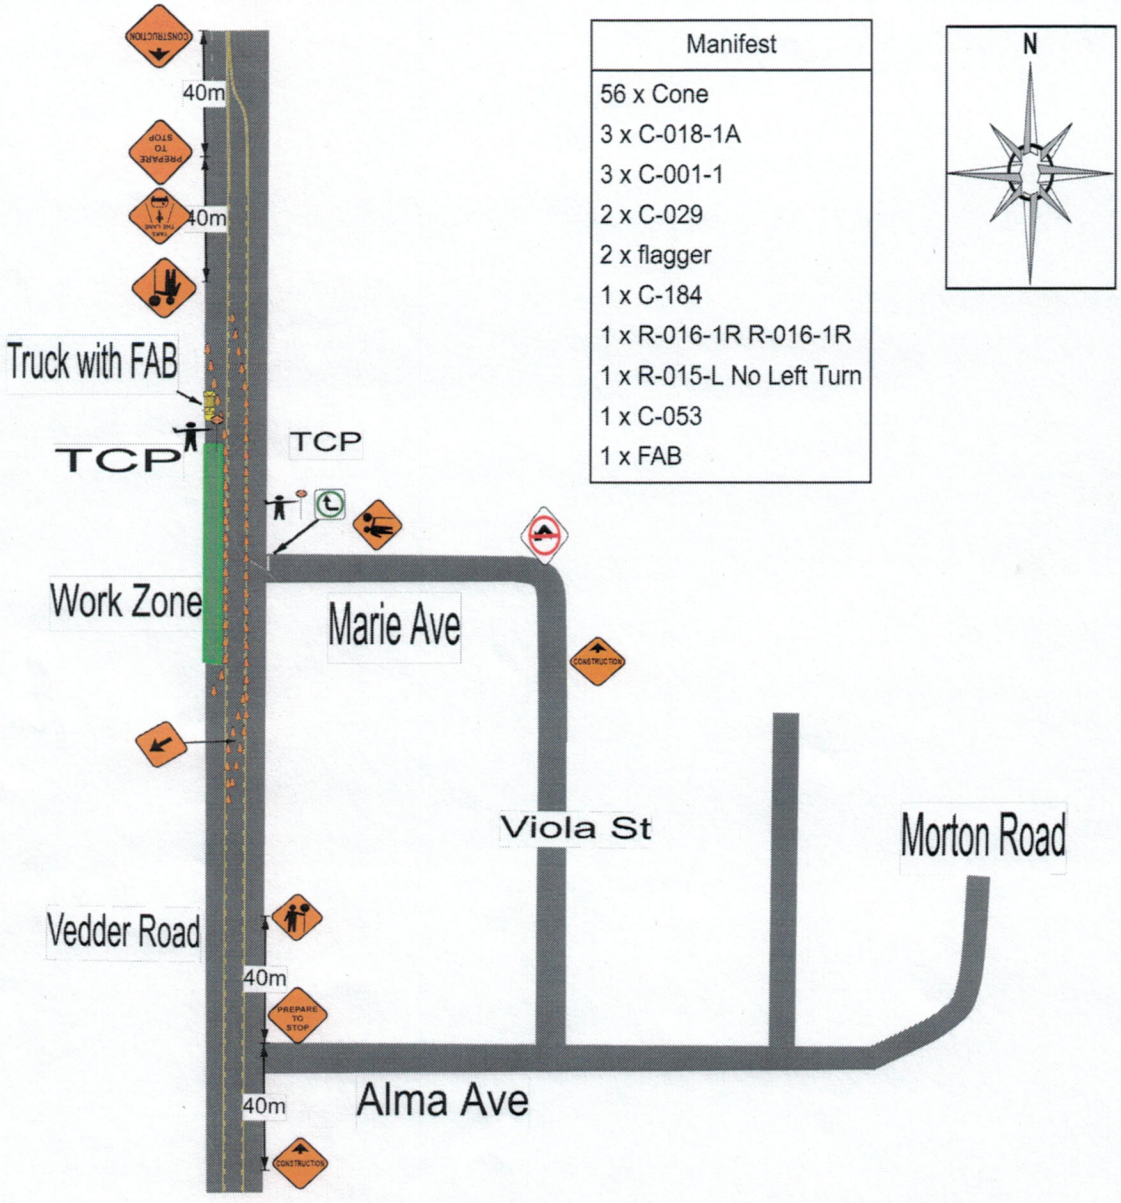

Manifest
56 x Cone
3 x C-018-1A
3 x C-001-1
2 x C-029
2 x flagger
1 x C-184
1 x R-016-1R R-016-1R
1 x R-015-L No Left Turn
1 x C-053
1 x FAB
